

Veltron Industries

CRM Transformation

Salesforce BA Final Project | Customertimes Corp 2026

Benedict Daxell Santoso

SF BA Consultant Trainee Program | June 2026



CRM Business Case

Why Veltron is investing in Salesforce | 3 Business Problems | Phase 1 Recommendation

PROBLEM 1 | COMMERCIAL OPERATIONS

Manual quoting creates multi-day cycle times and margin risk

- Reps build quotes manually in Excel using a PDF catalog.
- Deals above \$50K require email approval, adding 2–3 days. Complex configurations are frequently mis-quoted.

PROBLEM 2 | PARTNER CHANNEL

No channel visibility delays partner revenue by 6–8 weeks

- Distributors register deals by email with no status visibility and no standardized onboarding.
- 6–8 week activation cycle creates blind spots in partner pipeline forecasting.

PROBLEM 3 | FIELD SERVICE

Reactive field service creates SLA breach risk and churn exposure

- Technicians use phone assignments and paper work orders.
- No PM scheduling or SLA tracking. Platinum-tier equipment downtime is a direct churn risk.

PHASE 1 CLOUD RECOMMENDATIONS

Sales Cloud

Digitizes the full lead-to-quote cycle, replacing email and Excel with account management, CPQ, mobile access, and automated deal approvals.

Service Cloud

Replaces phone and paper with case management, mobile work orders, preventive maintenance scheduling, and SLA enforcement tied to customer contracts.

Experience Cloud

Converts the email-based distributor workflow into a structured Partner Portal for deal registration, onboarding, and performance tracking.

Salesforce Cloud & Feature Mapping

Sales Cloud

CPQ (Configure-Price-Quote)

Accurate quotes for complex equipment, no more PDF catalog + Excel

Approval Process

Deals above \$50K routed digitally, 2–3 day email wait eliminated

Opportunity Management

Real-time pipeline across NA & Europe, replaces spreadsheets

Salesforce Mobile App

Full field access on mobile, fixes core reason NA pilot was rejected

Account Tiering (Flow + Fields)

Auto-classifies Platinum / Gold / Silver by contract value

Service Cloud

Case Management

Structured case logging — no more phone intake where requests fall through

Work Order Management

Cases become assigned work orders — replaces paper dispatch

Entitlements & SLA Tracking

Contractual response times enforced — Platinum breach alerts automated

Field Service Mobile App

Work orders and job history on-site — paper eliminated entirely

Preventive Maintenance Scheduling

Scheduled visits from Installed Base data — reactive model replaced

Experience Cloud

Partner Deal Registration Portal

Self-service deal registration — replaces email-to-Channel-Manager

Guided Distributor Onboarding

Structured digital workflow — 6–8 week onboarding made repeatable

Customer Self-Service Portal

Cases and equipment docs online — call center volume reduced

Distributor Performance Dashboard

Real-time partner pipeline visibility — replaces manual Excel tracking

Content & Knowledge Library

Specs, pricing, and docs in one portal — email requests to internal teams eliminated

Stakeholder Register

Name / Role	Dept	Primary Interest	Engagement Approach
James Whitfield VP of Sales	Sales	Fast go-live; pipeline visibility	Primary sponsor. Weekly steering.
Rachel Okafor IT Director	IT	SAP integration first; data integrity	Engage early on integration design only.
David Chen CFO	Finance	Fixed budget; clear ROI	Dollars and risk only. No feature talk.
Maria Santos Sales Ops Manager	Sales	Forecast accuracy; clean pipeline data; data quality	★ Ground-level champion. Co-design from Day 1.
Tom Gallagher RSM North America	Sales	Mobile tool reps will use; post-pilot skeptic	⚠ Skeptic. Win him early — carries 5 reps.
Sophie Dubois RSM Europe	Sales	Europe pipeline visibility; parity with NA	Include in UAT. Can't feel like afterthought.
Kevin Park Service Director	Service	SLA compliance; PM scheduling	Champion for technician adoption.
Linda Reyes Channel Manager	Partner	Deal reg visibility; onboarding tracking	Involve in portal design from Day 1.
Alex Brennan Field Sales Rep (x9)	Sales	Tool that helps, not adds admin	WIIFM session pre-UAT. Make 1-2 champions.
Carlos Mendes Field Tech (x12)	Service	Simple mobile work orders	Mobile UAT. Pair with super-user.
Priya Nair Support Agent (x6)	Service	Case visibility; faster resolution	Natural early adopters. Involve in workshops.
Marco Ricci Distributor Contact	External	Self-service deal reg; status visibility	1-2 distributors in portal UX design.

POWER / INTEREST GRID

KEEP SATISFIED [High Power – Low Interest]

Rachel Okafor IT Director
David Chen CFO

MANAGE CLOSELY [High Power – High Interest]

James Whitfield VP of Sales
Maria Santos Sales Ops Manager ★
Tom Gallagher RSM North America 🇺🇸
Sophie Dubois RSM Europe
Kevin Park Service Director

MONITOR [Low Power – Low Interest]

KEEP INFORMED [Low Power – High Interest]

Linda Reyes Channel Manager
Alex Brennan Field Sales Rep (x9)
Carlos Mendes Field Tech (x12)
Priya Nair Support Agent (x6)
Marco Ricci Distributor Contact

Executive Sponsor: James Whitfield (VP Sales)

Authority and air cover to unblock roadblocks

Skeptic to convert first: Tom Gallagher (RSM NA)

win him before go-live and he carries his team.

Project Champion: Maria Santos (Sales Ops Mgr)

Owns the data, trusted by reps and leadership, no pilot baggage.

Co-design from Day 1 and she becomes Veltron's internal Salesforce authority.

Project Methodology Selection

Hybrid (Water-Scrum-Fall)

RECOMMENDATION: Hybrid (Water-Scrum-Fall) reconciles three conflicting constraints. Fixed budget + SAP gate = upfront scope control (Waterfall logic). VP urgency + skeptic risk from 2019 CRM failure = iterative visible wins (Agile logic). Hybrid brackets sprints inside a planned phase and a gated release.

PHASE 1 Discovery & Design

Weeks 1-6 | Waterfall Gate

Deliverables: Signed BRD, baselined scope, Installed Base mapped to SAP asset records, Maintenance Plan schema defined

Gate: CFO + IT Director co-sign before Sprint 1. SAP API readiness confirmed as Phase 1 exit criterion.

BA Artifacts: BRD, As-Is/To-Be maps, requirements classification

PHASE 2 Iterative Build

Weeks 7-16 | Agile Sprints

Sprint 1: Mobile Work Order capture screen for field technicians (replaces paper forms)

Sprint 2: Opportunity layout for North America sales team

Sprint 3: Service Case escalation view for Support Agents when PM schedule is missed

Sandbox: Mock SAP asset data enables user validation prior to live integration. Documented assumption; flagged for IT sign-off at Phase 1 gate.

PHASE 3 Integration, UAT & Deploy

Weeks 17-20 | Waterfall Gate

Deliverables: Live SAP endpoints connected, end-to-end UAT with key stakeholders

Gate: No production deployment without IT Director technical sign-off

Deferred: Experience Cloud portal, advanced CPQ, Europe channel rollout (each requires stable Phase 3 data)

RISKS & MITIGATION

Phase Creep: Scope freeze doc co-signed by CFO + VP Sales before Sprint 1. Major changes = Change Request; minor = next sprint. Knowing the difference is the BA's job.

SAP Delay:

SAP readiness locked as Phase 1 exit criterion at kickoff gate, not a Phase 3 discovery item.

DOCUMENTED ASSUMPTIONS

Fixed-price engagement assumed (scope creep directly erodes margin; CR gate is non-optional).

Client available for bi-weekly Sprint Reviews.

SAP live integration is Phase 3, not a Phase 1 blocker for user-facing build.

RACI Matrix

Activity	BA	PM	Solution Architect	Developer/Admin	Business Sponsor	IT Director	End User
Requirement Workshops with Business Stakeholders	A	C	C	I	C	I	R
Solution Design Sign Off	C	R	A	C	C	C	I
UAT Execution and Sign Off	R	C	C	R	A	C	R
Go-Live Decision	C	R	C	R	A	C	I
Post-go-live end user training delivery	A	R	I	R	C	I	R

A

Accountable: owns the outcome, one per row, answers if it fails

R

Responsible: does the work, can be shared


C

Consulted: two-way, input sought before decision

I

Informed: one-way, told after decision is made

As-Is Process Map: Lead to Quote

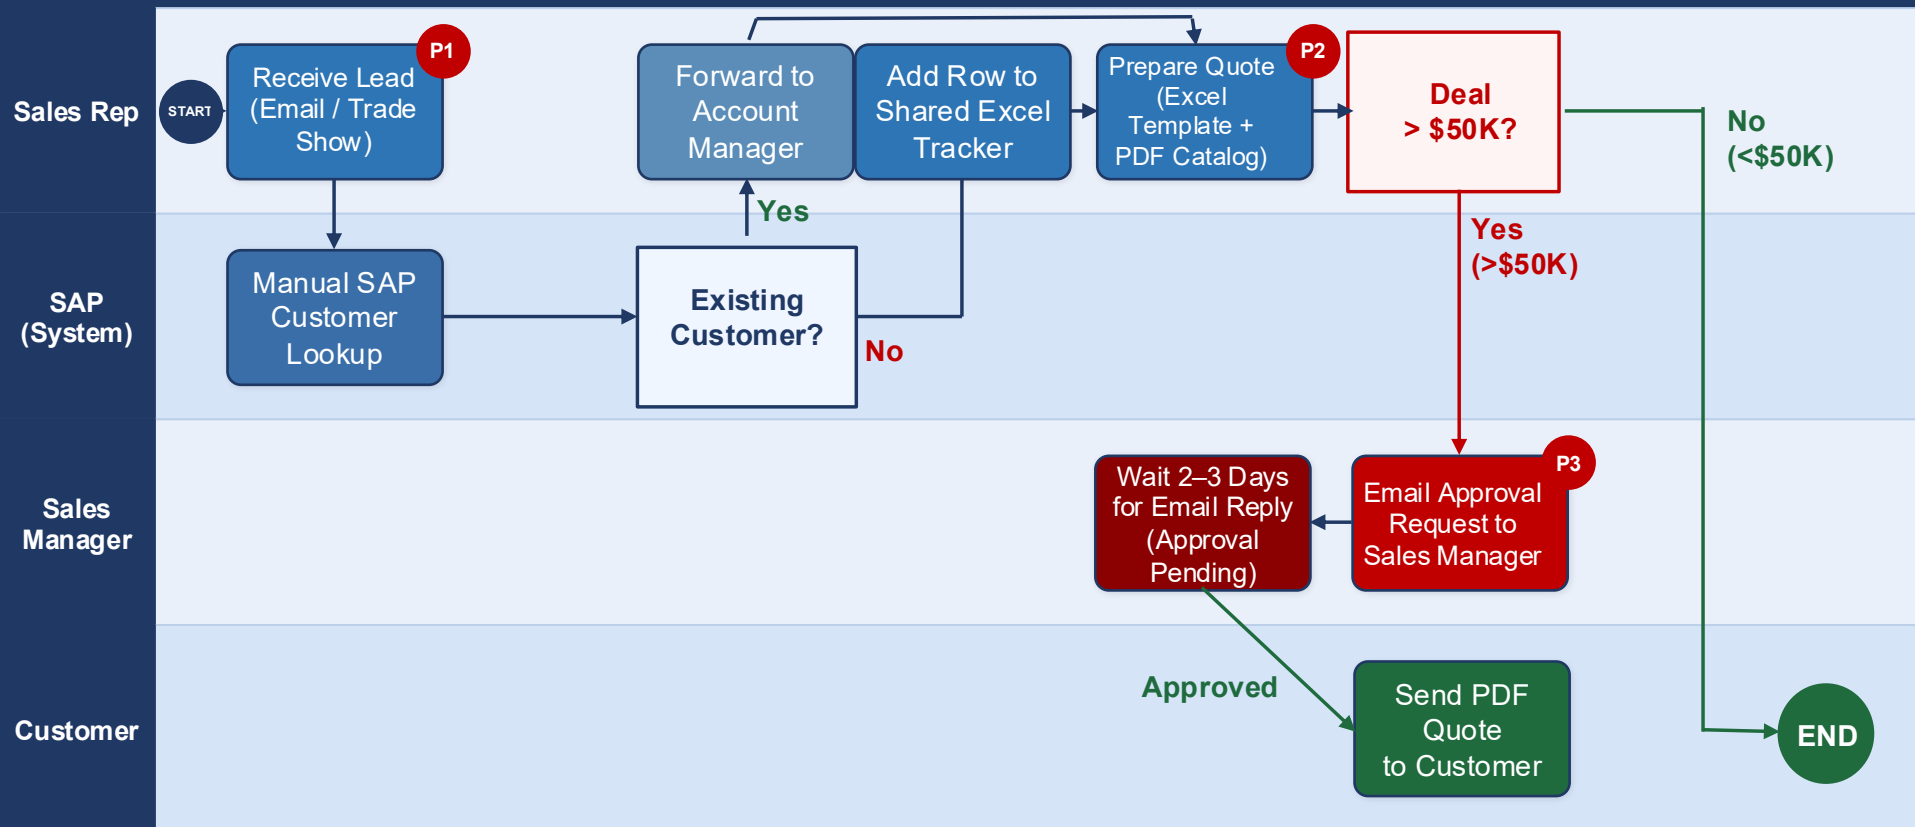


PAIN POINT LEGEND

P1 Unstructured Lead Capture — No system to log email/trade show leads; critical details lost, follow-ups missed, deals fall before pipeline entry.

P2 Manual Quoting from PDF Catalog — Wrong specs/SKUs/outdated pricing sent to precision-sensitive manufacturers; creates contract disputes & reputational damage.

P3 \$50K Approval Bottleneck — Quotes idle 2-3 days awaiting email reply; competitor displacement risk and eroded customer confidence.

To-Be Process Map

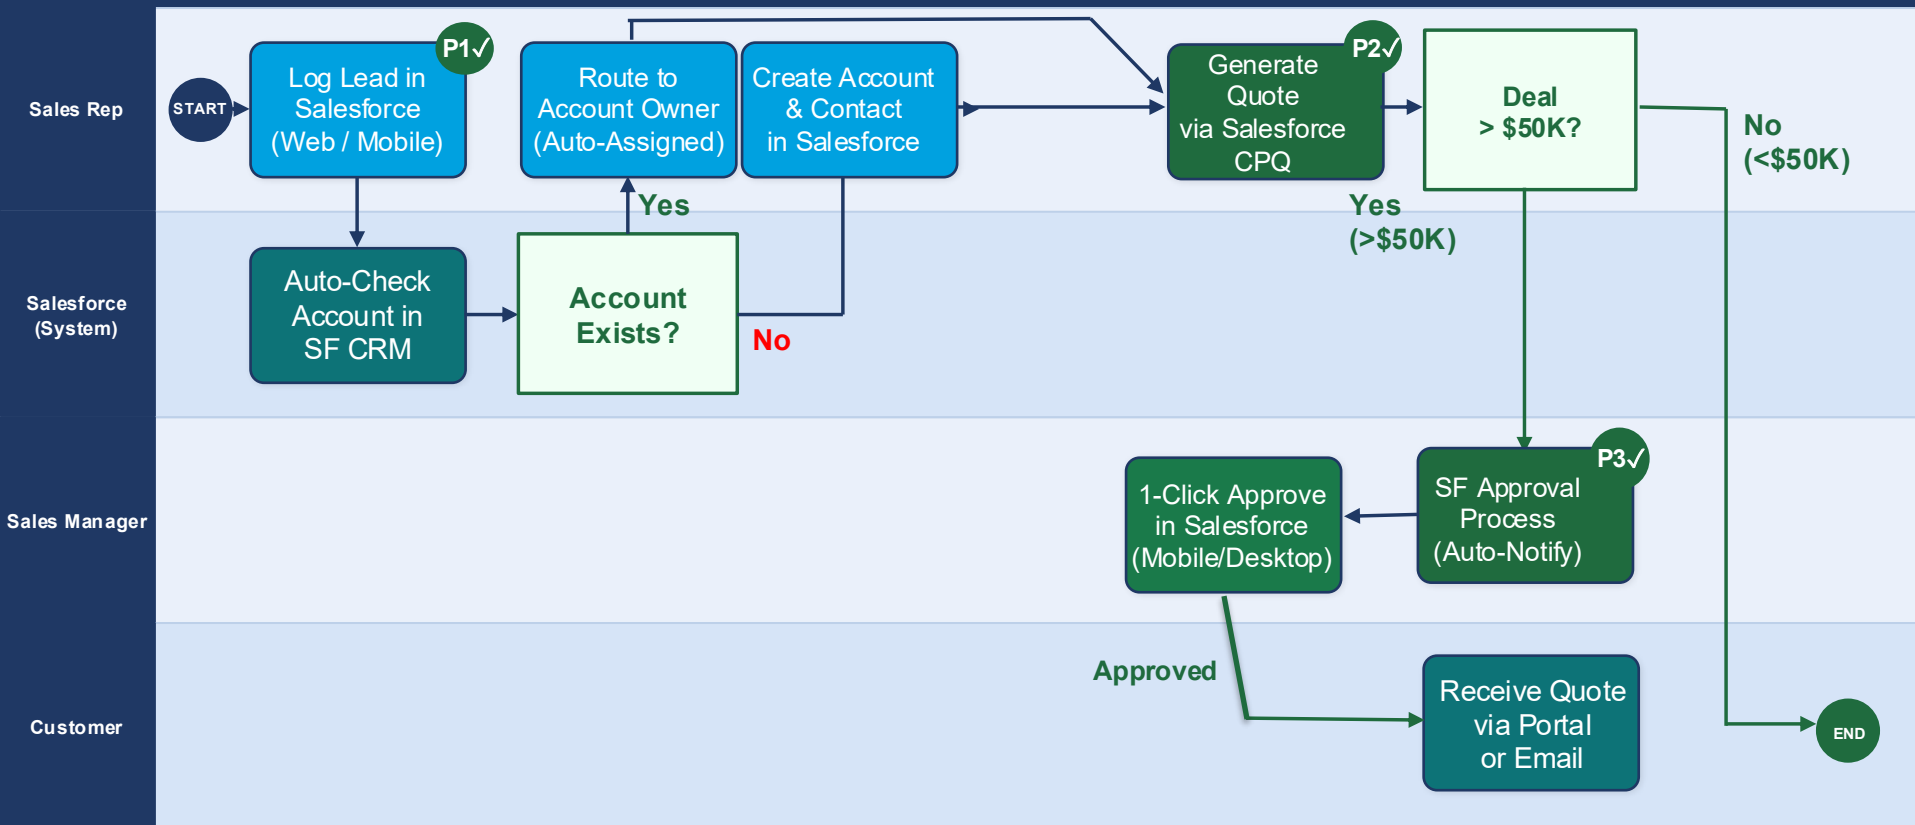

PAIN POINT RESOLUTIONS

- P1✓ Lead Capture → Salesforce Web/Mobile capture replaces email/trade show notes; all leads logged instantly with auto-dedup against existing accounts.
- P2✓ Manual Quoting → Salesforce CPQ auto-pulls product specs and pricing from a live catalog; eliminates PDF/Excel errors, cuts quote prep from hours to minutes.
- P3✓ Approval Bottleneck → SF Approval Process auto-notifies Sales Manager in-app and mobile; 1-click approval replaces 2–3 day email wait.

User Stories: Preventive Maintenance Scheduling (Epics + US-01 to US-03)

EPIC 1 Automated Maintenance Scheduling | Goal: Auto-generate Work Orders from asset usage & schedule thresholds | Stories: US-01, US-02, US-03

EPIC 2 Visibility & Customer Communication | Goal: Real-time maintenance visibility for teams & Platinum customers | Stories: US-04, US-05

US-01 Epic 1 Service Director

As a Service Director, I want a dashboard of assets due for preventive maintenance in the next 30 days, so that I can allocate technician capacity before SLA deadlines are breached.

AC1 Happy Path

Given an Asset has a Maintenance Due Date, When the Service Director opens the dashboard, Then all Assets due within 30 days are displayed sorted by due date ascending.

AC2 Alternate Path

Given a Work Order already exists for an Asset's upcoming cycle, When the dashboard loads, Then that Asset is marked Scheduled and removed from the unassigned queue.

AC3 Edge Case — Zero State

Given no Assets are due within 30 days, When the dashboard loads, Then a zero-state message displays: 'No assets due for maintenance in the next 30 days.'

US-02 Epic 1 Field Service Technician

As a Field Service Technician, I want to receive a mobile work order with asset location, equipment history, and service checklist before I arrive on site, so that I can complete the visit without contacting the office.

AC1 Happy Path

Given a Work Order is assigned in Salesforce, When the technician opens the SF Field Service mobile app, Then the Work Order shows site address, equipment model, last service date, and the maintenance checklist.

AC2 Alternate Path

Given the technician completes all checklist items, When they mark the Work Order Complete, Then the Asset's Last Service Date and Next Maintenance Due Date auto-update in Salesforce.

AC3 Edge Case — Site Access Failure

Given the equipment is inaccessible on site, When the technician sets status to Cannot Complete with a reason code, Then the Service Director is auto-notified and a follow-up task is created.

US-03 Epic 1 Service Director

As a Service Director, I want Salesforce to auto-create a Work Order when asset usage hours exceed the maintenance threshold or the scheduled date is reached, so that no equipment goes past its service interval without a work order.

AC1 Happy Path — Usage Trigger

Given an Asset's Usage Hours meets or exceeds the Maintenance Interval threshold, When the scheduling Flow runs, Then Salesforce auto-creates a Work Order with status New and priority High.

AC2 Alternate Path — Date Trigger

Given an Asset has a Maintenance Due Date and no open Work Order, When today equals that date, Then Salesforce automatically creates a Work Order for that Asset.

AC3 Edge Case — Missing Usage Data Blocks Auto-Scheduling

Given an Asset's Usage Hours field has not been updated in 14+ days, When the Flow runs, Then a data quality alert is sent to the Service Director and no Work Order is created.

User Stories: Preventive Maintenance Scheduling (US-04, US-05 +Dependencies + INVEST)

US-04

Epic 2

Customer Support Agent

As a Customer Support Agent, I want to see the maintenance schedule and Work Order history for any customer asset from the Account or Case record, so that I can answer service inquiries without switching between systems.

AC1 Happy Path

Given a customer asks about their next scheduled maintenance, When the Agent opens the Account record, Then all linked Assets display Last Service Date, Next Maintenance Due Date, and current Work Order status.

AC2 Alternate Path — Escalation

Given a customer escalates about a missed visit, When the Agent opens the Asset record, Then the full Work Order history is visible with timestamps and technician name.

AC3 Edge Case — In-Flight Work Order Lookup

Given an Asset has an active Work Order, When the Agent views it, Then the technician name and estimated completion date are visible to share with the customer.

US-05

Epic 2

Customer (Platinum Tier)

As a Platinum tier Customer, I want to receive an automated notification when a preventive maintenance visit is scheduled for my equipment, so that I can plan site access and avoid production disruptions.

AC1 Happy Path

Given a Work Order for a Platinum Asset moves to Scheduled status, When the status change is saved, Then Salesforce auto-sends an email to the primary contact with the date, technician name, and estimated duration.

AC2 Alternate Path — Reschedule

Given the scheduled date changes, When the Work Order is updated in Salesforce, Then the customer automatically receives a revised notification with the new date.

AC3 Edge Case — SLA Breach Escalation

Given a Platinum Asset has no Work Order within 5 days of its Maintenance Due Date, When the threshold is breached, Then an escalation alert fires to the Service Director.

STORY DEPENDENCY & RELATIONSHIP TABLE

Story	Depends On	Reason	Related To
US-01	US-03	Dashboard requires Work Orders from US-03 to be meaningful	US-04
US-02	US-03	Technician Work Orders must exist before mobile delivery is possible	US-01
US-03	None	Foundation story — scheduling Flow is source of all Work Orders	US-01, US-02
US-04	US-03	Support Agent view requires Work Order history on Asset records	US-01, US-05
US-05	US-03	Customer notification triggers on Work Order status change from US-03	US-04

Sprint sequence: US-03 (Flow foundation) → US-01 (visibility) → US-02 (mobile) → US-04 (support) → US-05 (customer notification)

INVEST COMPLIANCE

- I Independent** Each story ships standalone. US-05 deferred to Sprint 5 without blocking US-02 in Sprint 3.
- N Negotiable** AC thresholds (30-day window, 5-day SLA) negotiated with Service Director — not hardcoded.
- V Valuable** Every story maps to a measurable outcome: SLA adherence, technician efficiency, or Platinum retention.
- E Estimable** Each story scopes to one SF object and one action. Dev team can size without ambiguity.
- S Small** Each story fits one 2-week sprint. No story requires multi-epic or multi-object builds simultaneously.
- T Testable** Every AC uses Given/When/Then with explicit conditions and observable system outputs.

Business Rules Definition

Tool Key:

Scheduled Flow

Record-Triggered Flow

Validation Rule

Assignment Rule

BR-01

Scheduled Flow

Auto-Generate Work Order on Threshold Breach

Rule When an asset's usage hours meet or exceed its maintenance interval, or today equals the Maintenance Due Date, Salesforce must automatically create a linked Work Order.

Why this tool Requires time-based batch evaluation across all Asset records with conditional child-record creation — the exact pattern Scheduled Flow is designed for. Validation Rules cannot create records. Assignment Rules apply only to Leads/Cases. Approval Processes require human initiation.

If not enforced Equipment exceeds its service interval with no Work Order in the system. Undetected wear leads to unplanned breakdowns, SLA breaches for Platinum clients, and potential contractual liability. Preventive maintenance reverts to reactive maintenance.

BR-03

Record-Triggered Flow

Auto-Assign Work Order to Technician by Territory

Rule When a Work Order is created, it must be automatically assigned to the Field Service Technician whose service territory matches the asset's site location.

Why this tool Assignment Rules apply only to Leads and Cases — they cannot route Work Orders. Record-Triggered Flow fires on Work Order creation, performs a cross-object lookup (Asset → Territory → User), and updates the Owner field instantly without user action.

If not enforced Work Orders sit unassigned in an unowned queue. Service Directors manually assign every Work Order, reintroducing the bottleneck Salesforce was meant to eliminate. Wrong-territory dispatching increases travel cost and delays maintenance visits.

BR-02

Validation Rule

Work Order Cannot Be Closed Without Service Notes

Rule A Field Service Technician must not be able to mark a Work Order as Complete unless the Service Notes field is populated with details of the work performed.

Why this tool Blocks a bad data save — the definition of a Validation Rule use case. Fires on record save, checks field presence given a status value, and prevents save if the condition fails. A Flow could do this but is over-engineered for a simple field-presence check on save.

If not enforced Work Orders are closed with no record of what was done. Asset service history becomes unreliable. If equipment fails post-visit, Veltron has no audit trail for root cause analysis or liability defense.

BR-04

Scheduled Flow


Escalate to Service Director When SLA Is At Risk

Rule If a Platinum tier Asset has no scheduled Work Order within 5 business days of its Maintenance Due Date, Salesforce must automatically send an escalation alert to the Service Director.

Why this tool Requires time-based batch evaluation across Platinum Assets with conditional notification — Scheduled Flow running daily (e.g. 6am). Record-Triggered Flow does not fire on time passage alone. Validation Rules cannot send notifications. Approval Processes need human initiation.

If not enforced Platinum clients approach their due date with no visit scheduled. No internal alert fires. The date passes, maintenance is missed, and the client discovers the breach themselves; triggering SLA penalties, account escalation, and Platinum tier churn risk.

Data Model: ERD + Standard Objects (Accounts, Assets, Work Order)

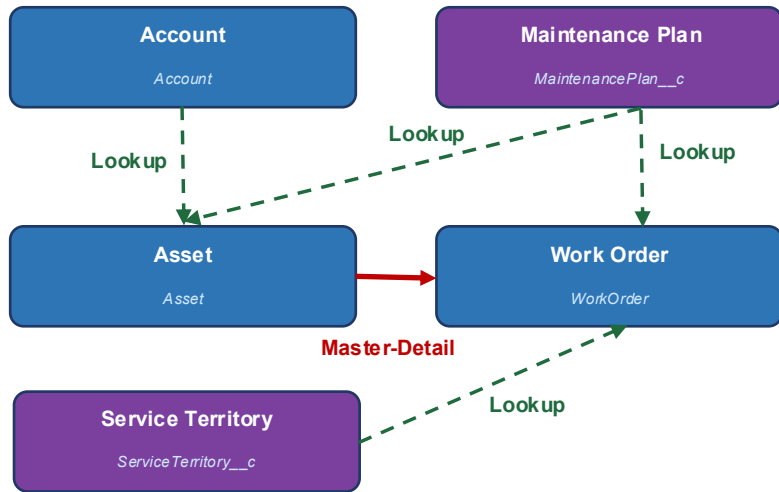

RELATIONSHIP JUSTIFICATIONS

Account → Asset [Lookup] Asset (installed equipment) can exist without the Account if the customer relationship ends. Service history must be preserved even after account deletion.

Asset → Work Order [Master-Detail] A Work Order is a child event of a specific Asset. It has no meaning without the Asset it services. Deleting an Asset should cascade-delete its Work Orders to prevent orphaned records.

MaintenancePlan → Asset [Lookup] A Maintenance Plan defines a schedule template. The Asset is referenced but can exist independently of any plan.

MaintenancePlan → Work Order [Lookup] A Work Order is generated by a Maintenance Plan but must persist even if the plan is modified or archived. Loose link preserves the historical record.

ServiceTerritory → Work Order [Lookup] Territory is an assignment reference. A Work Order must survive territory restructuring; it should not be deleted if Veltron redraws regional boundaries.

Object Type Key:

Custom Object (__c)

Master-Detail (child cannot exist without parent)

Standard Object

Lookup (child independent of parent)

Field Name	Data Type	Required	Business Purpose
ACCOUNT (Standard)			
Account Name	Text	Y	Veltron customer company name — primary identifier
Industry	Picklist	N	Automotive / High-Tech / Industrial — for segmentation
Account_Tier__c	Picklist	Y	Platinum / Gold / Standard — drives SLA escalation rules
ASSET (Standard)			
Asset Name	Text	Y	Equipment identifier e.g. VTX-5000-SN1234
Usage_Hours__c	Number	N	Running counter; triggers BR-01 maintenance threshold
Maintenance_Due_Date__c	Date	Y	Next service date; second trigger condition for BR-01
Maintenance_Interval__c	Number	Y	Hours between required services per equipment spec
Last_Service_Date__c	Date	N	Auto-updated by Flow when Work Order marked Complete
WORK ORDER (Standard)			
Status	Picklist	Y	New / Scheduled / In Progress / Complete / Cannot Complete
Service_Notes__c	Long Text	N	Required on save when Status = Complete — enforces BR-02
Priority	Picklist	Y	High / Medium / Low — auto-set High by scheduling Flow
Assigned_Technician	Lookup:User	Y	Field tech assigned via territory-matching Flow (BR-03)

Data Model: Custom Objects + Design Decisions (Maintenance Plan, Service Territory)

Field Name	Data Type	Required	Business Purpose
MAINTENANCE PLAN (Custom)			
Plan_Name__c	Text	Y	Schedule name e.g. VTX-5000 Annual Inspection
Frequency__c	Picklist	Y	Monthly / Quarterly / Annual / Usage-Based
SLA_Tier__c	Picklist	Y	Platinum / Gold / Standard — links to BR-04 escalation
SERVICE TERRITORY (Custom)			
Territory_Name__c	Text	Y	Region identifier e.g. Northeast US, Southeast Asia
Assigned_Technician__c	Lookup:User	Y	Default technician for BR-03 territory matching
Coverage_Postcode__c	Text	N	Postcode range used as matching condition in Flow

DESIGN DECISIONS & ASSUMPTIONS

D-001 Work Order as Standard Object

- Salesforce includes a native Work Order object with built-in status fields, Field Service mobile integration, and scheduling tools.
- Using the standard object inherits all of this without custom builds or additional licensing complexity.

D-002 Account Tier as Custom Field on Account

- Account_Tier__c is a custom field added to the standard Account object rather than a standalone object.
- This keeps tier information at the account level where it is most accessible to Flows, Validation Rules, and reporting; no additional object complexity required.

D-003 Service Territory as Custom Object

Assumption:

- Veltron's org does not have Salesforce Field Service (FSL) licensed.
- If FSL is in scope, ServiceTerritory__c should be replaced with the native FSL Service Territory object and BR-03 Flow updated accordingly.
- Must be validated with the Solution Architect before build.

D-004 Only One Master-Detail Relationship

- The brief does not require Master-Detail everywhere. Only Asset → Work Order qualifies — a Work Order has no independent existence without its Asset.
- All other child objects (Asset, Maintenance Plan reference, Service Territory reference) have legitimate reasons to survive parent deletion.
- Defaulting to Master-Detail across the board would create a fragile data model.

Security & Access Design: Preventive Maintenance Scheduling

Mechanism Key:

OWD (Org-Wide Default)

Role Hierarchy

Permission Set

Sharing Rule / Sharing Set

Experience Cloud

SR-01 Technician Work Order Isolation

Persona: Field Service Technician

OWD

Role Hierarchy

Criteria Sharing Rule

A Field Service Technician must only view and edit Work Orders assigned to them — no lateral visibility to other technicians' records.

Why OWD = Private on Work Order blocks all lateral access by default. Role Hierarchy gives Service Directors upward visibility. A Criteria Sharing Rule then shares each Work Order with its assigned technician specifically.

If not enforced Technicians see each other's work orders, exposing customer site locations and equipment schedules across a multi-client manufacturing environment.

SR-02 Service Director Full Visibility

Persona: Service Director

Role Hierarchy

A Service Director must view, edit, and report on all Work Orders across all territories and technicians without restriction.

Why With OWD = Private on Work Order, the Role Hierarchy automatically grants upward access. Placing Service Director above all technician roles is sufficient — no sharing rule needed, which keeps the security model clean and auditable.

If not enforced Service Directors cannot see cross-territory Work Orders. Scheduling gaps go undetected and Platinum SLA breaches are missed before the escalation window closes.

SR-03 Support Agent Read-Only Access

Persona: Customer Support Agent

Permission Set

A Customer Support Agent must read any Asset and Work Order to answer service inquiries, but must not create or edit Work Orders directly.

Why A Permission Set grants Read-only on Work Order and Asset without elevating the full profile. OWD = Public Read Only on Asset gives all internal users view access. Separation of duty is preserved — no write access to service records.

If not enforced Support Agents cannot see asset or work order history without switching systems, which lead to slower call handling, inaccurate information, and eroded customer trust.

SR-04 Field Sales Rep Territory Isolation

Persona: Field Sales Rep

OWD

Role Hierarchy

A Field Sales Rep must only view and edit Accounts and Opportunities they own — no visibility to records owned by reps in other territories.

Why OWD = Private on Account and Opportunity restricts lateral access between reps. Role Hierarchy gives Sales Managers upward visibility to their team without sharing rules. This is the standard Salesforce design for territory-based sales orgs.

If not enforced Reps see each other's accounts and pipeline. Territory disputes arise, Platinum accounts are exposed to unauthorized reps, and Veltron faces GDPR and data governance exposure.

SR-05 External Customer Portal Isolation

Persona: External Customer (Platinum / Gold / Standard)

OWD

Experience Cloud

Sharing Set

An external customer logging into the Veltron Experience Cloud portal must only see their own Account, Assets, and linked Work Orders — zero cross-customer visibility.

Why External users operate outside the internal role hierarchy. OWD External = Private blocks cross-customer access by default. A Sharing Set scoped to Account = current user's account automatically grants each customer access only to their own records — scales as new customers onboard.

If not enforced A Platinum customer can view a competitor's equipment list and service schedule — a critical data breach with direct legal and contractual consequences in a B2B manufacturing context.

Reports & Dashboard Design: Sales Performance Dashboard — 4 Report Specifications

Report Type Key:**Summary — grouped totals****Matrix — 2D cross-tab****Tabular — flat record list***Monday Morning Frame — VP of Sales asks: What is in our pipeline? Are we hitting forecast? Who is winning? Which deals are stalled?***R-01****Summary****Active Pipeline by Stage and Region**

Objects & Fields Opportunity: Name, Stage, Amount, Close Date, Owner, Region; Account: Account Tier

Groupings Primary: Stage | Secondary: Region

Filters Close Date = current quarter; Stage ≠ Closed Won or Closed Lost; Amount > 0

Business Question What is the total value of our active pipeline at each stage, by region? Where are deals accumulating or stalling?

R-02**Summary****Sales Forecast vs Quota by Rep**

Objects & Fields Opportunity: Amount, Forecast Category, Close Date, Owner; User: Name, Role, Region, Quota__c

Groupings Primary: Owner (Rep) | Secondary: Forecast Category (Commit / Best Case / Pipeline)

Filters Close Date = current quarter; Stage ≠ Closed Lost

Business Question For each rep, how does forecasted revenue compare to quarterly quota? Which reps are on track and which are at risk?

R-03**Matrix****Opportunity Win Rate by Rep and Industry**

Objects & Fields Opportunity: Stage, Amount, Close Date, Owner; Account: Industry

Groupings Rows: Owner (Rep) | Columns: Account Industry (Automotive / High-Tech / Industrial)

Filters Close Date = last 90 days; Stage = Closed Won or Closed Lost only

Business Question Which reps are winning at the highest rate and in which industry verticals? Are we underperforming in any specific sector?

R-04**Tabular****Overdue Opportunities (Stalled Pipeline)**

Objects & Fields Opportunity: Name, Stage, Amount, Close Date, Owner, Last Activity Date, Days_Overdue__c (formula); Account: Name, Account Tier

Groupings None — flat record list sorted by Days Overdue descending

Filters Close Date < today; Stage ≠ Closed Won or Closed Lost; sorted by Days Overdue desc

Business Question Which open deals have passed their expected close date? Which Platinum accounts are at risk from stalled opportunities?

Reports & Dashboard Design: Dashboard Components + Dynamic Regional Configuration

Component Type Key:

Funnel/Bar Chart

Gauge

Table

C-01 Funnel Chart Pipeline Funnel by Stage

Source: R-01: Active Pipeline by Stage and Region

Visualizes Total pipeline value at each deal stage for the current quarter. Visual funnel shape reveals where volume concentrates and where it drops — bottlenecks are visible in seconds.

Why this component A VP reads the funnel shape without reading a table. Narrow top = insufficient leads. Wide middle, narrow bottom = closing problem. Diagnosis on first glance.

C-02 Gauge Forecast vs Quota Gauge

Source: R-02: Sales Forecast vs Quota by Rep

Visualizes Total committed forecast for the current quarter as a percentage of regional quota. Gauge needle position shows whether the region is on track (green zone) or at risk (red zone).

Why this component One number with a visual scale is more actionable on Monday morning than a row of percentages. Green zone = proceed. Red zone = intervention needed. No analysis required.

C-03 Table Win Rate by Industry Table

Source: R-03: Opportunity Win Rate by Rep and Industry

Visualizes Win rate percentage and Closed Won amount per industry vertical (Automotive, High-Tech, Industrial). Shows where Veltron is strong and where it is losing deals it should be winning.

Why this component Win rate by industry needs exact percentages, not visual approximations. A bar chart loses the precision the Sales Ops Manager needs to report upward. Table preserves the numbers.

DYNAMIC DASHBOARD CONFIGURATION — Regional Manager View

The Problem with Standard Dashboards

- A standard dashboard runs as a fixed named user (every viewer sees the same data regardless of who they are).
- A Regional Sales Manager in Northeast would see pipeline from all regions, not just their own.
- This defeats the purpose of a regional performance view.

The Dynamic Dashboard Solution

- A Dynamic Dashboard runs as 'the logged-in user' instead of a fixed user.
- When the Northeast Manager opens the dashboard, Salesforce executes all 4 reports as that manager (applying their Role Hierarchy and OWD = Private on Account and Opportunity automatically).
- The reports return only Northeast data with zero additional filters needed.

Configuration Steps

- Open the dashboard → Properties → Change 'View Dashboard As' from a named user to 'The logged-in user' → Save.
- Each Regional Manager now sees their own region's pipeline, forecast, win rate, and stuck deals automatically on every open.

Dependency & Limitation

- Requires OWD = Private on Account and Opportunity with role hierarchy correctly configured (Task 11 SR-04).
- Limitation: Dynamic Dashboards support up to 5 simultaneous running users in Enterprise Edition and 10 in Unlimited Edition.
- Validate with Solution Architect if Veltron scales beyond this.

Change Impact Assessment: Veltron CRM Rollout

G-01 Field Sales Reps

Resistance: No WIIFM + Loss of Control

What Changes

Process: Email leads + Excel tracker + manual PDF quoting replaced by Salesforce Lead capture, CPQ quoting, and full pipeline visibility.

Tools: Excel and email replaced by Sales Cloud and CPQ.

Behavior: Every lead, quote, and interaction becomes a traceable record. No more opaque spreadsheets.

T1: Before/After Demo with a Real Veltron Deal

Run a side-by-side walkthrough of a real automotive client inquiry through the old Excel process vs Salesforce CPQ. Quantify the time difference: quote prep drops from 45 minutes to 8. WIIFM must be personal and tangible, not a corporate efficiency pitch.

T2: Convert the Most Resistant Rep into the CRM Champion

Identify the rep who pushed back hardest during the failed pilot. Bring them in 4 weeks pre-launch as a UAT co-designer with authority to request one implemented change. When peers see the loudest critic switch sides, trust transfers faster than any training session.

Assumption The failed CRM pilot involved Field Sales Reps. If distributor partners were also affected, G-03 resistance is significantly higher and requires executive co-sponsorship before portal launch.

G-02 Field Service Technicians

Resistance: Loss of Competence

What Changes

Process: Paper work orders and phone-based site info replaced by SF Field Service mobile app with pre-loaded asset history and checklists.

Tools: Paper forms and phone calls replaced by SF Field Service mobile.

Behavior: Must complete digital checklists and add service notes before closing. BR-02 blocks incomplete Work Order closure.

T1: Peer Super-User Pairing for First 10 Field Visits

Train one technician per territory as a super-user 3 weeks before go-live. Pair every technician with their territory super-user for their first 10 live work orders. Learning happens on site in context with no public failure risk, not in a classroom.

T2: Show Technicians Their Own Service History at Onboarding

Pre-load all Asset records with migrated service history before training. Open a real asset record the technician has serviced before and show their own historical work on screen. Makes the benefit immediate: the system already knows their work and is built to help them.

G-03 Distributors and Channel Partners

Resistance: Low Trust + Change Fatigue

What Changes

Process: Deal registration via email and phone status updates replaced by Veltron Experience Cloud portal for self-service submission and tracking.

Tools: Email chains replaced by the partner portal.

Behavior: Must use a structured submission form and check the portal for status instead of waiting for email replies.

T1: 30-Day Read-Only Portal Access Before Mandatory Submission

Give partners portal access 30 days before email submission is retired. They submit via email as usual but can log in to see their existing deals in the portal. By the time the portal is mandatory, they have already seen their data correctly. Trust is earned before compliance is required.

T2: Partner Success Story Bulletin After First 60 Days

Identify the first 2 to 3 distributors whose portal-submitted deals were approved faster than the email baseline. Publish a one-page bulletin via email with specific time comparisons: portal approval in 2 hours vs 3-day email average. Peer-driven proof beats vendor reassurance every time.

Adoption and Training Plan: Go-Live Approach and Timeline

RECOMMENDATION

Phased Rollout

Phase 1: NA Sales (Sales Cloud + CPQ)
Phase 2: Field Service (FSL + Work Orders)
Phase 3: Distributors (Experience Cloud Portal)

Big Bang

REJECTED

All users go live simultaneously. With reps who already rejected a prior CRM pilot, a visible failure collapses the entire initiative. Fixed budget cannot absorb remediation.

Another Pilot

REJECTED

Veltron already ran a failed pilot. A second pilot signals 'they are trying this again' to the sales team. The political damage equals the operational risk.

Phased Rollout

SELECTED

Fits all 3 constraints: contains initial risk for skeptics, limits budget to one group, gets Phase 1 live faster than org-wide rollout. Each phase generates quick wins for the next.

ADOPTION TIMELINE: 4 WEEKS PRE GO-LIVE TO 4 WEEKS POST GO-LIVE

Week	Phase	Key Activities	Key Output
W-4	Pre	Identify and train super-users. Run Before/After Demo with most resistant Sales Rep. Communicate Phase 1 go-live date to all affected users.	3 to 5 trained champions ready per user group
W-3	Pre	Role-based training for Phase 1 Sales Reps: Lead capture, account lookup, CPQ quoting only. Distribute one-page role-specific cheat sheets.	Every Phase 1 user completes role-specific training
W-2	Pre	UAT with super-users and converted champion rep. Fix critical bugs. Update cheat sheets based on feedback.	UAT sign-off from champion rep and Service Director
W-1	Pre	Data migration validation. Confirm all Accounts, Contacts, and Opportunities migrated correctly. Brief Sales Managers on dashboard access.	Data confirmed clean. Sales Managers briefed.
W1	Live	Phase 1 goes live. Super-users available on-call. Service Director monitors dashboard daily. Log all support tickets.	All Phase 1 users logged in and submitted at least one record
W2	Hyper	Daily check-in with super-users. Triage support tickets: training issue vs system bug. Targeted re-training for anyone not yet proficient.	Support ticket volume trending down
W3	Hyper	First adoption metrics review: login rate, Opportunity data completeness, quote cycle time. Share results with VP of Sales.	Metrics baseline established. VP of Sales briefed.
W4	Post	Publish Partner Success Story Bulletin. Announce Phase 2 start date. Begin Phase 2 super-user training.	Phase 2 preparation starts. Phase 1 momentum maintained.

Adoption and Training Plan: Metrics and Change Model

1 Login and Active Usage Rate

Measures Percentage of Phase 1 Sales Reps logging in at least 4 times per week AND creating or updating at least one Opportunity or Lead record per session. Login alone is not adoption.

How Salesforce Login History report combined with Opportunity and Lead activity reports filtered by Created Date and Last Modified Date. Run weekly. Target: 80% active by end of Week 3.

Why Veltron Distinguishes reps who are complying with minimum access from reps actually working in the system. Only the latter delivers business value and validates the Lead-to-Quote redesign.

2 Opportunity Data Completeness Rate

Measures Percentage of Opportunity records created in Salesforce with all required fields populated: Stage, Amount, Close Date, Account, and Forecast Category.

How Salesforce report on Opportunities created in the last 30 days filtered by missing required fields. Run weekly. Target: 90% completeness rate by Week 4.

Why Veltron If reps are creating Opportunities with blank Amount and Close Date, the Sales Performance Dashboard from Task 12 is meaningless. This metric directly validates whether the VP of Sales can trust the pipeline view.

3 Quote Cycle Time Trend

Measures Average number of days from Lead creation to Quote sent. Compared month-over-month against the pre-Salesforce baseline established from Excel records.

How Salesforce Summary report on Leads and linked Opportunities using a custom formula field calculating cycle time in days. Baseline from Excel records in final 30 days pre-go-live. Target: 20% reduction by Month 2.

Why Veltron The business outcome metric. The entire Lead-to-Quote redesign in Tasks 6 and 7 was built to reduce the manual quoting cycle. If cycle time is not improving, adoption is technical but not operational.

CHANGE MODEL: ADKAR (Prosci)

Why ADKAR fits Veltron

Veltron's resistance is individual-level, not org-wide culture. Field Sales Reps who rejected the prior CRM pilot each resisted for their own specific reason: no personal benefit, fear of pipeline exposure, distrust of the system. ADKAR is designed to diagnose exactly this pattern by moving each individual through Awareness, Desire, Knowledge, Ability, and Reinforcement as sequential building blocks.

Why not the others

Kotter

Designed for org-wide top-down transformation with executive sponsorship. Veltron's resistance is at the individual rep level, not organizational. Too heavyweight for a fixed budget rollout.

Lewin

Useful diagnostic lens but too high-level to be actionable. Tells you where you are in the cycle but not what to do about each individual's specific resistance type.

Bridges

Focuses on emotional transition and identity loss. Relevant for Field Service Technicians but ADKAR covers this through the Desire and Reinforcement stages and is more actionable across all 3 Veltron groups.

ADKAR to Veltron Technique Mapping

A - Awareness

Before/After Demo with a real Veltron deal scenario

D - Desire

Convert the most resistant rep into the CRM Champion

K - Knowledge

Role-based training and one-page cheat sheets per role

A - Ability

Super-user pairing for first 10 field visits per territory

R - Reinforcement

3 adoption metrics tracked weekly plus Partner Success Bulletin

Veltron Business Problems and Salesforce Solution

VELTRON'S KEY BUSINESS PROBLEMS

01

Revenue leaks in the quote cycle

Reps build complex quotes by hand from a PDF catalog in Excel. Quotes take days, contain errors, and large deals wait 2 to 3 days for email approval.

Outcome: CPQ quoting, days to hours, near-zero error rate

02

Partner revenue arrives 6 to 8 weeks late

Distributors register deals by email with no status visibility and no self-service. Onboarding a new partner takes 6 to 8 weeks of channel revenue trapped in a queue.

Outcome: Self-service partner portal, onboarding under 1 week

03

Reactive service threatens Platinum accounts

Field service responds only after equipment breaks. No preventive maintenance scheduling. For Platinum clients (over \$500K), a missed SLA is a churn and penalty event.

Outcome: Preventive maintenance, Platinum SLA compliance over 95%

PROPOSED SOLUTION SCOPE (PHASE 1)

Sales Cloud

Fixes slow quoting and zero pipeline visibility

CPQ quoting, mobile app for field reps, opportunity tracking, approval for deals over \$50K, customer tiering

Service Cloud

Fixes reactive, SLA-breaching field service

Preventive maintenance scheduling, work order assignment, Field Service mobile, SLA tracking, case management

Experience Cloud

Fixes the 6 to 8 week partner onboarding delay

Distributor deal registration, partner self-service onboarding, customer case portal, documentation access

Deferred to Phase 2+: EU/APAC rollout, customer self-service portal, Einstein AI forecasting, inventory management, contract lifecycle. Deferring protects the fixed budget; each item has a phase to return in.

Roadmap, Risks, KPIs and Next Steps

IMPLEMENTATION ROADMAP

Phase 0

Mo 1-2

SAP integration foundation (gated)

Phase 1

Mo 3-4

Sales Cloud + CPQ go-live (quick win)

Phase 2

Mo 5-6

Service Cloud + preventive maintenance

Phase 3

Mo 7-8

Experience Cloud partner portal

Milestone: SAP integration gated first. No data goes live until IT signs off.

EXPECTED OUTCOMES AND KPIs

KPI	Baseline	Target
Quote cycle time	Days	Hours
Forecast accuracy	Manual	Over 85%
Platinum SLA compliance	Reactive	Over 95%
Distributor onboarding	6-8 weeks	Under 1 week
Quote error rate	High	Near zero

TOP 3 RISKS AND MITIGATION

Skeptic disengagement (prior failure)**Fix:** Convert loudest critic to champion; land a Phase 1 quick win to rebuild trust by proof.**SAP integration delay blocks go-live****Fix:** Gate SAP as Phase 0 with IT sign-off; sequenced first so it cannot surprise us later.**Scope creep erodes fixed budget****Fix:** Fixed-scope-per-phase envelope; new requests triaged to a future phase, not Phase 1.

RECOMMENDED NEXT STEPS (INTO ANALYSIS)

1

Approve Phase 1 scope and fixed budget

Exec Sponsors

2

Confirm SAP integration requirements with IT

IT + BA

3

Baseline KPIs from current Excel records

Sales Ops + BA

4

Stand up the champion network for adoption

BA + Change Lead
