

VELTRON INDUSTRIES

Salesforce CRM

Transformation

Executive Discovery Readout

Prepared for: VP of Sales, CFO, IT Director

Presented by Customertimes | Conclusion of Discovery
Phase



Veltron's engineering leads the market. Its commercial operations do not. Salesforce closes that gap in three phases.

Days to Hours

QUOTE CYCLE TIME

Complex equipment quotes that take days today
move to same-session CPQ generation.

6-8 Wks to Days

DISTRIBUTOR ONBOARDING

Partner portal self-service replaces the email-and-
wait registration backlog.

Reactive to Planned

FIELD SERVICE MODEL

Preventive maintenance scheduling protects
Platinum SLAs before equipment fails.

What we are asking you to approve today

1. A phased rollout that protects the fixed budget and proves value before scaling org-wide.
2. SAP integration delivered as the gated foundation, so no customer data goes live unverified.
3. A measurable business case tied to quote speed, forecast accuracy, and Platinum retention.

Three structural gaps are costing Veltron revenue, margin, and customer trust right now.

01

Revenue leaks in the quote cycle

Reps build complex equipment quotes by hand from a PDF catalog in Excel. Quotes take days, contain errors, and large deals wait 2 to 3 days for email approval. Deals stall and margin erodes on every misquote sent to an automotive or high-tech client.

02

Partner revenue arrives 6 to 8 weeks late

Distributors register deals by emailing the Channel Manager with no status visibility and no self-service. Onboarding a new partner takes 6 to 8 weeks. Channel revenue that should be flowing is trapped in an email queue.

03

Reactive service threatens Platinum accounts

Field service responds only after equipment breaks. There is no preventive maintenance scheduling. For Platinum clients (over \$500K annual value) a missed SLA is a churn and contract-penalty event, and today nothing prevents it.

Every problem maps to a measurable target you can hold us accountable to.

Business Problem	Target Outcome	KPI	Baseline to Target
Slow, error-prone quoting	Faster, accurate CPQ quotes	Quote cycle time	Days to hours
No pipeline / forecast visibility	Reliable forecasting for the VP	Forecast accuracy	Manual to >85%
6-8 week partner onboarding	Self-service partner portal	Onboarding time	6-8 wks to <1 wk
Reactive field service	Preventive maintenance scheduling	Platinum SLA compliance	Reactive to >95%
Manual Excel reporting	Live executive dashboards	Report prep time	Hours to real-time

Targets are directional and will be baselined with Veltron's sponsors during the Analysis phase.

Three Salesforce Clouds, each tied to a specific Veltron revenue problem, not a feature wish-list.

Sales Cloud

Fixes slow quoting and zero pipeline visibility

- CPQ for complex equipment quoting
- Mobile app for field reps
- Opportunity and pipeline tracking
- Automated approval for deals over \$50K
- Customer tiering (Platinum/Gold/Silver)

Service Cloud

Fixes reactive, SLA-breaching field service

- Preventive maintenance scheduling
- Work order creation and assignment
- Field Service mobile for technicians
- SLA tracking per customer contract
- Case management for breakdowns

Experience Cloud

Fixes the 6-8 week partner onboarding delay

- Distributor deal registration portal
- Partner self-service onboarding
- Customer case submission portal
- Equipment documentation access
- Channel performance visibility

We protect the fixed budget by shipping a focused Phase 1 and consciously deferring the rest.

IN PHASE 1 - Go Live Fast


- ✓ **SAP integration foundation**
- ✓ Sales Cloud + CPQ for NA direct sales
- ✓ Service Cloud with preventive maintenance
- ✓ Experience Cloud distributor portal
- ✓ Core dashboards: pipeline, forecast, SLA
- ✓ Mobile for field reps and technicians

DEFERRED - Phase 2 and Beyond

- EU and APAC regional sales rollout
- Customer self-service portal (Tier 2)
- Advanced AI forecasting and Einstein
- Field service inventory and parts management
- Contract lifecycle management
- Marketing Cloud integration

Deferring is a decision, not an omission. Each deferred item has a business reason to wait and a phase to return in.

A phased delivery that gates SAP integration first and lands a sales quick win to rebuild trust.

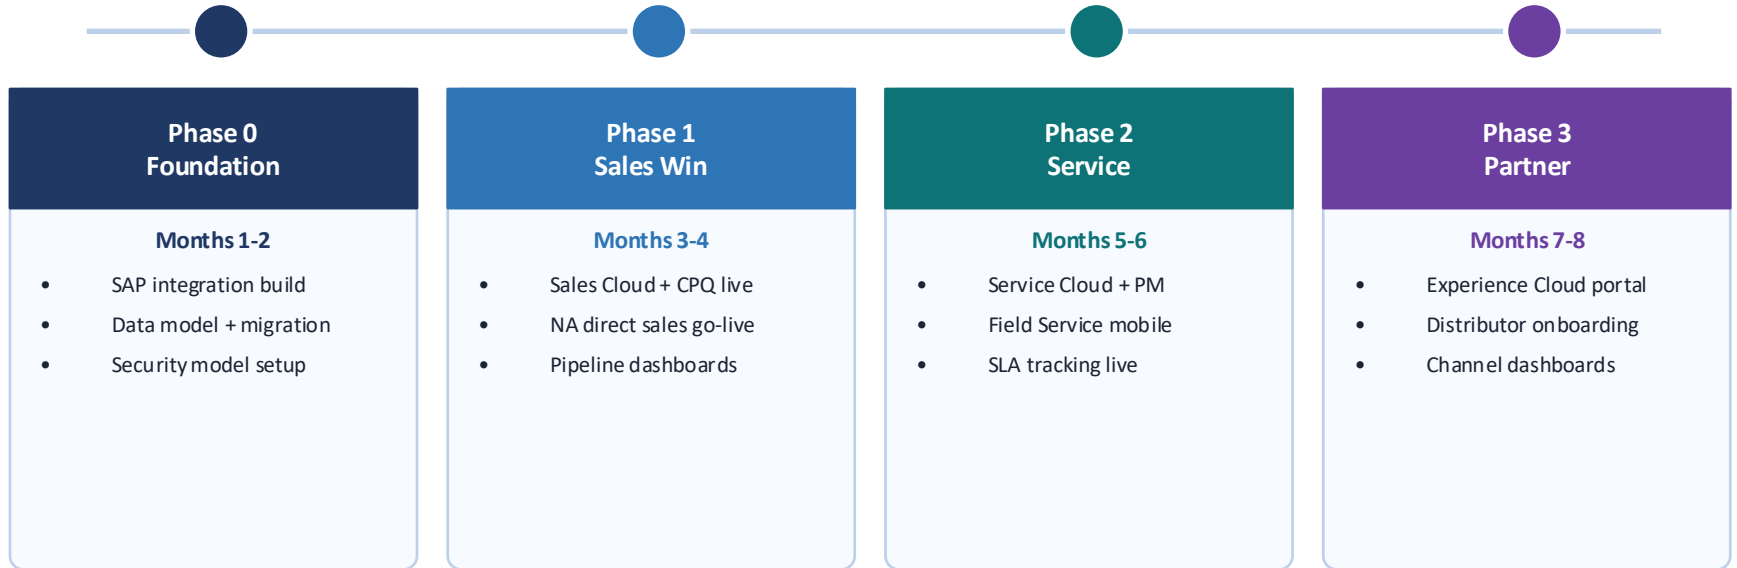

Key milestone: SAP integration (Phase 0) is gated. No customer data goes live in Salesforce until IT signs off. This directly answers the IT Director's condition.

We see three risks clearly and have a mitigation for each. None of them are reasons to wait.

R1 Skeptic disengagement after the prior failure

High Severity

Mitigation: Convert the most resistant rep into a co-design champion during UAT. Land a visible Phase 1 sales quick win before asking anyone to trust the system. Trust is rebuilt by proof, not promises.

R2 SAP integration delay blocks go-live

High Severity

Mitigation: Gate SAP integration as Phase 0, before any sales data migrates. Treat it as the foundation milestone with IT sign-off. The dependency is sequenced first, so it cannot surprise us later.

R3 Scope creep erodes the fixed budget

Medium Severity

Mitigation: Fixed-scope-per-phase envelope with a documented deferred list. Every new request is triaged into a future phase, not absorbed into Phase 1. The budget is protected by structure, not willpower.

Five KPIs give the CFO a clear ROI line and the VP of Sales a weekly scoreboard.

KPI	Baseline	Target	Owner
Quote Cycle Time	Days	Hours	VP of Sales
Forecast Accuracy	Manual / unreliable	>85%	VP of Sales / CFO
Platinum SLA Compliance	Reactive	>95%	Service Director
Distributor Onboarding	6-8 weeks	<1 week	Channel Manager
Quote Error Rate	High (manual)	Near zero (CPQ)	Sales Ops

Baselines confirmed with the primary sponsor at Analysis kickoff. We measure the trend, not a single launch-day number.

A hybrid, phased delivery with adoption baked in from day one, not bolted on at go-live.

Delivery Methodology

- **Hybrid: plan-driven phase gates, Agile sprints inside each phase**
- Fixed scope per phase protects the CFO's budget
- SAP integration gated in Phase 0 satisfies IT's condition
- Early sales quick win delivers the VP's urgency and rebuilds trust

Adoption Strategy (ADKAR)

- **Phased rollout, not Big Bang, given skeptics and fixed budget**
- Convert the loudest critic into a co-design champion
- Super-user pairing for technicians moving to mobile
- Measured weekly: usage rate, data completeness, quote cycle time

Four moves take us from Discovery into Analysis in the next two weeks.

1

Approve Phase 1 scope and budget

Sign-off from VP of Sales, CFO, and IT Director on the scope shown today and the fixed-budget phase envelope.

Executive Sponsors

2

Confirm SAP integration requirements

IT Director workshop to lock the integration scope and data-quality rules before the Phase 0 build begins.

IT Director + BA

3

Baseline the KPIs

Capture current quote cycle time, forecast accuracy, and SLA figures from existing Excel records to set measurable targets.

Sales Ops + BA

4

Stand up the champion network

Identify and recruit champions per group, starting with the most skeptical reps from the prior pilot.

BA + Change Lead

THE ASK

Approve Phase 1 today. We will return at Analysis with a baselined business case and a working SAP integration plan.

Why now: Every week of delay is another week of days-long quotes, trapped partner revenue, and unprotected Platinum SLAs. The engineering reputation Veltron built over 25 years deserves commercial operations that match it.
